Bar Chart for Improvements to roads and drains at Kogilu, Agrahara, Hegdenagar and surrounding area in Ward No 05 and 06 Byatarayanapura sub division Package-02

Bill: Second and Part Bill

Name of Agency :- Benaka Developers & Project Pvt.Ltd.

Sl.No	Description of work	BOQ Quantity	Upto date Quantity	Work Completed (%)
1	KSRRB 300-1. Earthwork excavation by manual means for roads, drains & similar works in	8443.14	6,937.78	82.00
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) (P.No.27, I.No.5.33 of PW,	5845.36	3,297.09	56.00
3	Removing and resetting of footpath slab (P.No.270, I.No.37.56 of PW, P&IWTD SR 2018-19)	753.30	753.30	100.00
4	Providing granite Slabs of Selected quality roughly dressed and fixed in cement mortor (1:6) including	3313.48	2,266.25	68.00
5	KSRRB M2900-1. Plain cement concrete M10 mix with crushed stone aggregate 40mm nominal	9.24	2.82	31.00
6	Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar &	9.72	9.72	100.00
7	Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs. with	2.16	2.16	100.00
8	34.17 Providing and laying in position plain/Reinforced cement cement concrete M20 for sub	24.64	0.00	0.00
9	KSRRB M2200-6. Providing T.M.T. steel reinforcement for R.C.C. work including	1.97	0.00	0.00
10	Providing and laying 100mm thick pre-cast cover slabs over drains of width not exceeding 800 mm using	83.70	0.00	0.00
11	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm	88.80	31.20	35.00
12	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including	19892.00	18,943.64	95.00
13	KSRRB M400-17. Providing, laying, spreading and compacting crushed stone aggregates of granite /	15960.30	15,355.29	96.00

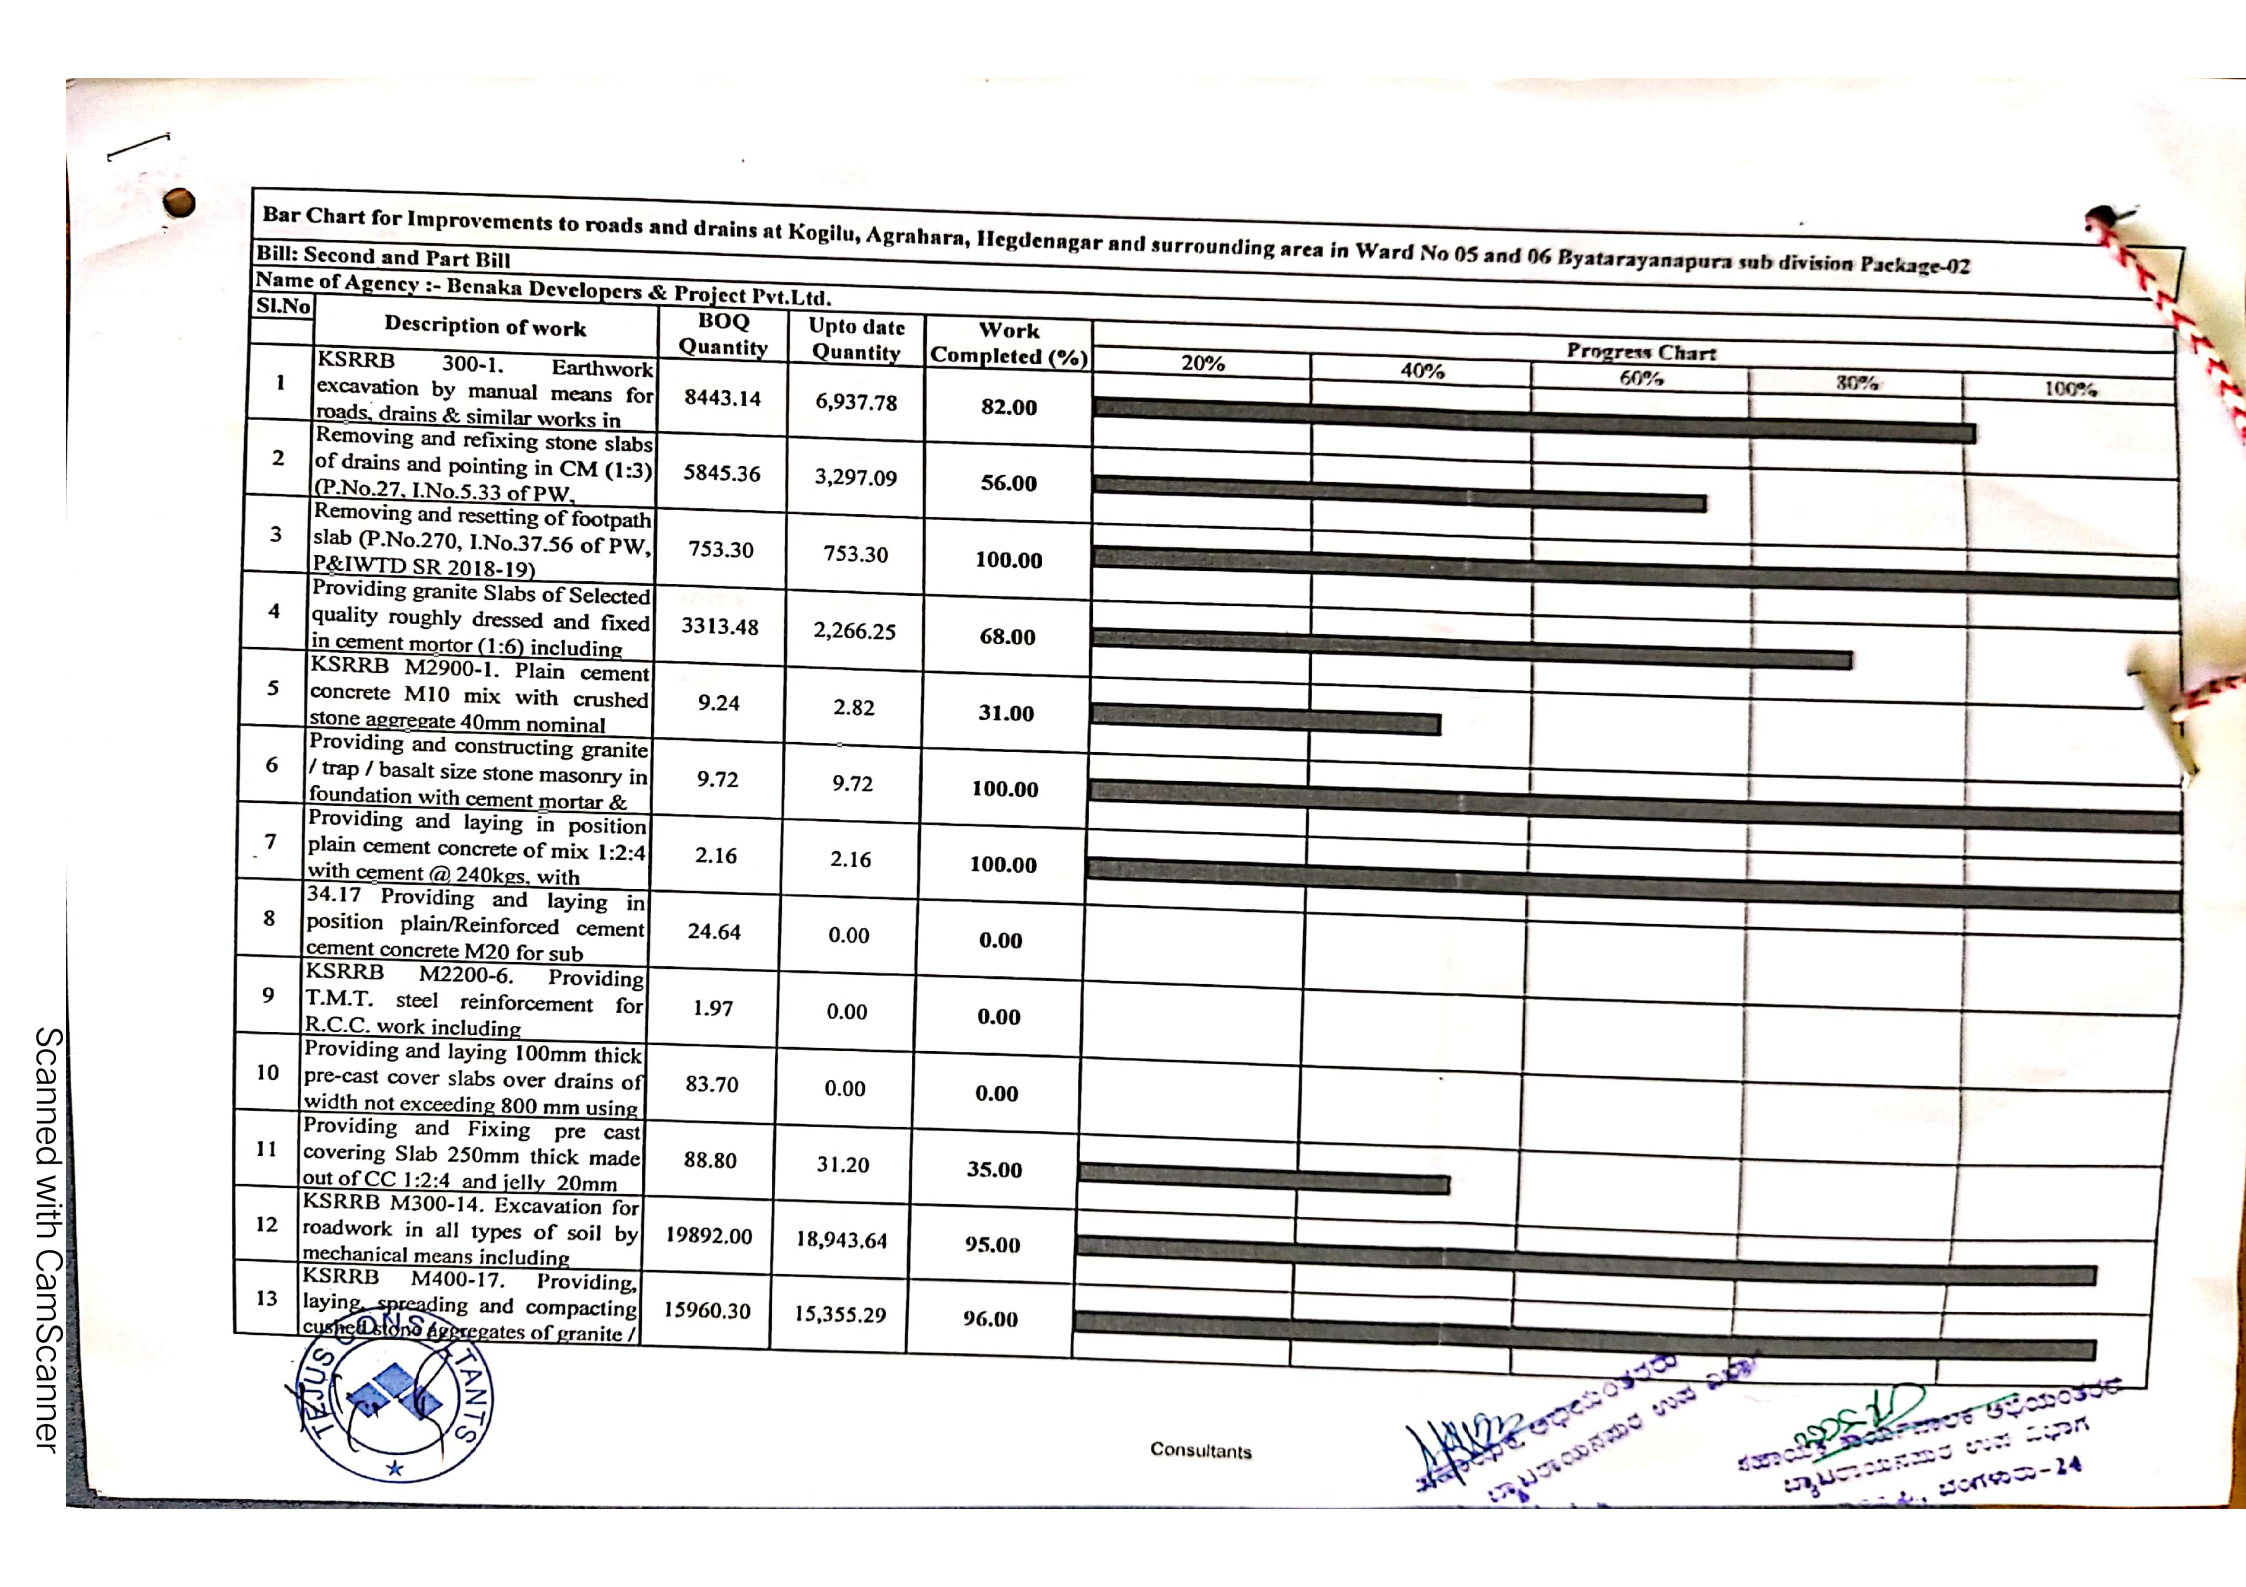

Consultants

Scanned with CamScanner

Sl.No	Description of work	BOQ Quantity	Upto date Quantity	Work Completed (%)	Progress Chart				
					20%	40%	60%	80%	100%
14	KSRRB M 500-6, Providing and applying primer coat with SS bitumen emulsion on prepared	63841.30	0.00	0.00					
15	KSRRB 500-2: Cleaning the existing black topped surface with brooms, soft brushes and finally	48492.70	0.00	0.00					
16	KSRRB M500-7 : Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared	140091.00	0.00	0.00					
17	KSRRB M500-17. Providing and laying dense graded bituminous macadam using crushed aggregates	1387.84	0.00	0.00					
18	Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of	4493.36	0.00	0.00					
19	KSRRB M800-13.Road Marking with Hot Applied Thermoplastic Compound with Reflectrising	4370.50	0.00	0.00					
20	KSRRB M600-1. Construction of dry lean cement concrete mix CC1:5:10 with OPC cement	369.82	235.34	64.00					
21	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M30 with	369.82	0.00	0.00					

TEJUS CONSULTANTS

Consultants

Scanned with CamScanner
